


2024 Upcoming Works Timeline

While we've had a major push before Christmas and opened up for shopping over this busy period, we still have some work to complete. This final push will see us complete the project at least 6 months ahead of schedule.

Please see the timeline below for a summary of the work remaining in 2024.

For more information about the development project, visit www.totallygeorgious.nz or please contact Ged Casey Communications Advisor gcasey@isaac.co.nz | 027 201 8621

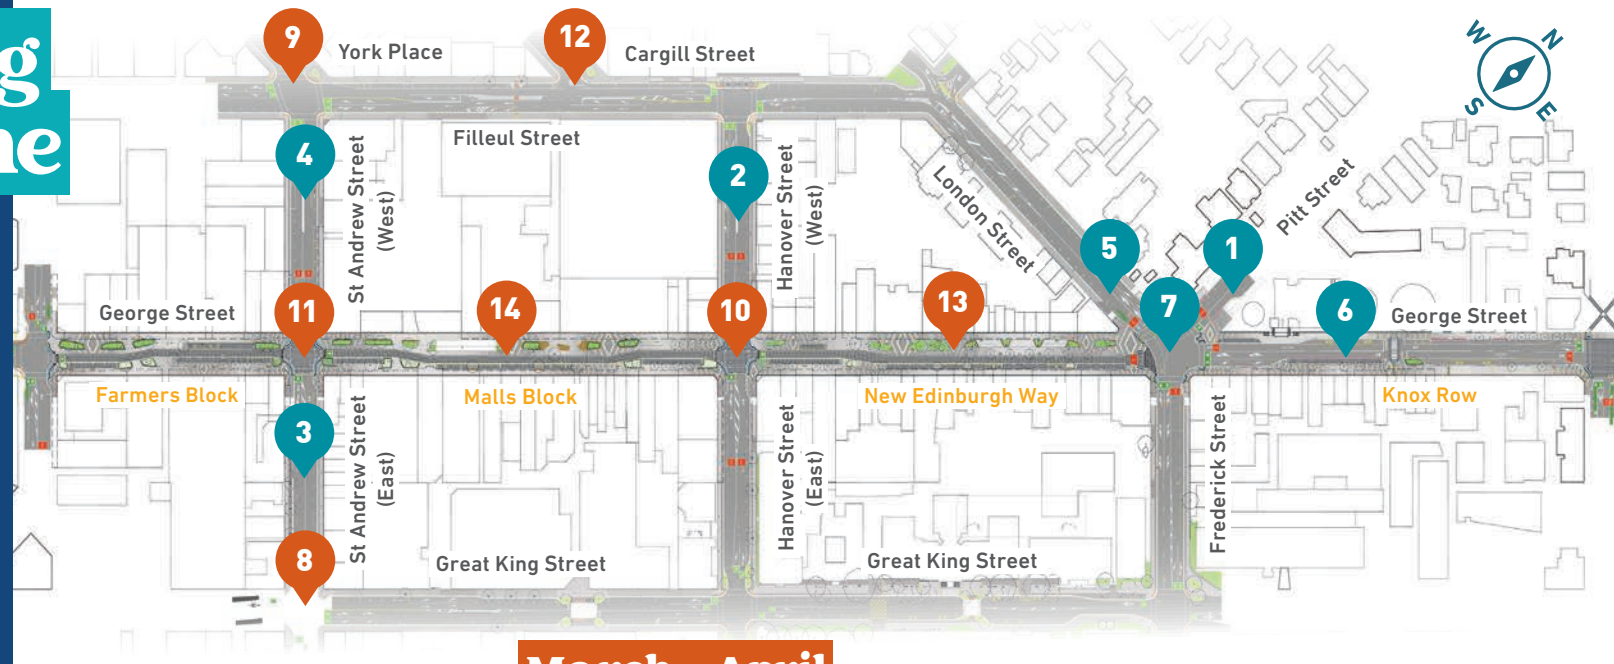

January - February

- 1 Pitt Street (Southern side)**
Work: Installation of new kerb
Traffic management: Pitt Street reduced to one lane.
Timing: Early January - February
- 2 Hanover Street (West)**
Work: Complete deep trenching to replace broken sewer line.
Traffic management: Road reduced to one lane.
Timing: Mid January - Mid February
- 3 St Andrew Street (East)**
Work: Completion of water connections and installation of paving.
Traffic management: Road shoulder and parking closed. Pedestrians redirected.
Timing: Mid January - Mid February
- 4 St Andrew Street (West)**
Work: Installation of paving
Traffic management: Road shoulder and parking closed. Pedestrians redirected.
Timing: Mid January - Early February

- 5 London Street/Frederick Street**
Work: Installation of new kerb.
Traffic management: No road closures, some traffic disruptions may occur.
Timing: Late January - Early February
- 6 Knox Row**
Work: Widening build out on church side, re-marking of bus stops and installation of bus shelters.
Traffic management: Road shoulder closed.
Timing: Early February - Mid February
- 7 5 Way Intersection**
Work: Installation of new road surface.
Traffic management: Intersection will be closed at nights.
Timing: Mid February - Late February

March - April

- 8 Great King Street/St Andrew Street Intersection**
Work: Connection of completed underground pipes.
Traffic management: One lane closed.
Timing: Late February - exact dates TBC
- 9 York Place Intersection**
Work: Completion of underground service.
Traffic management: Varying lane closures.
Timing: February - April
- 10 Hanover Street/George Street Intersection**
Work: Preparation and installation of paving.
Traffic management: Intersection closed during this time.
Timing: Early March - exact dates TBC
- 11 St Andrew Street/George Street Intersection**
Work: Preparation and installation of paving.
Traffic management: Intersection closed during this time.
Timing: Early March - exact dates TBC

- 12 Filleul/York/Cargill Streets**
Work: Minor above ground transport works.
Traffic management: Temporary road shoulder closures/partial parking removal.
Timing: Mid March - April TBC
- 13 New Edinburgh Way**
Work: Completion of paving, installation of above ground infrastructure and gardens.
Traffic management: Block closed to traffic. Motel/car parking access will remain. Access will change direction to Frederick Street, to allow completion of southern end of block.
Timing: Expected completion early April
- 14 Malls Block - Manaaki Space and Stages**
Work: Installation of Manaaki Space, stage platforms and additional street furniture.
Traffic management: Road shoulders closed.
Timing: End of April

Note: There will be teams working throughout the area over the coming months on final tidy-up works.
